

Ecodan® Residential Extended Warranty Process


(herein referred to as “Extended Warranty Process”)

I. Purpose


- A. This Extended Warranty Process is a guide to completing the procedure for a contractor to request and obtain extended parts warranty for Ecodan® and approved Heat-flo storage tank products.
- B. Items that must be submitted to apply for extended warranty are:
 1. System Design pdf through Ecodan® System Sizer
 2. Completed Ecodan® Startup Check List including all product Model and Serial numbers, installing contractor name and address, name of contractor employee who has completed the required Ecodan® Residential Essentials or Ecodan® Residential Installation Overview course, end customer name and address, date of installation and startup.
 3. Submit aforementioned documents via email within 90 days of the startup date to cmwarranty@hvac.mea.com

II. Ecodan® System Sizer

- A. After building the system in the Ecodan® System Sizer select the “View Design Report” button from the bottom of the screen.

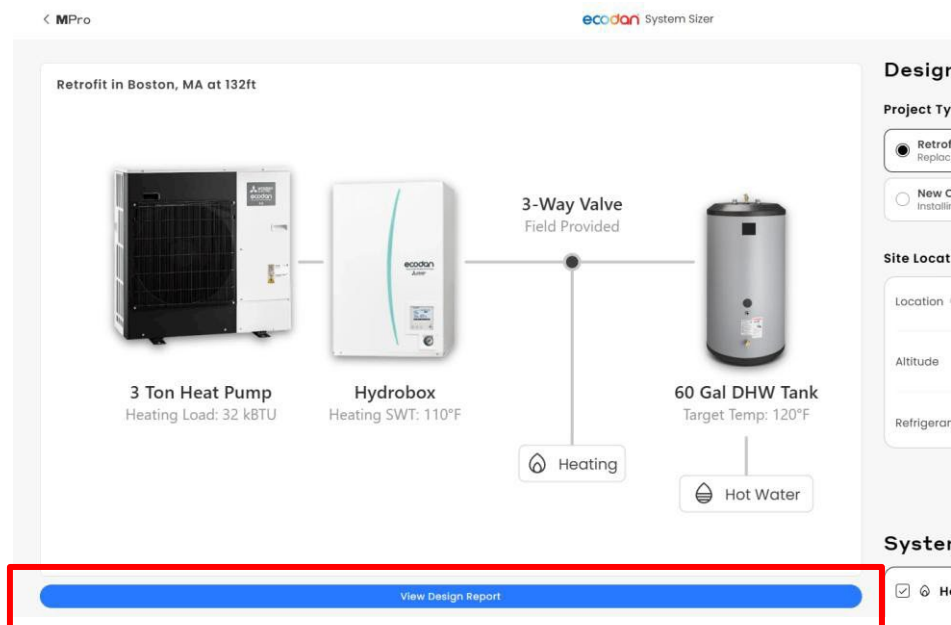

- B. You can then select either the download icon  or the ellipsis icon  from the top right of the window.

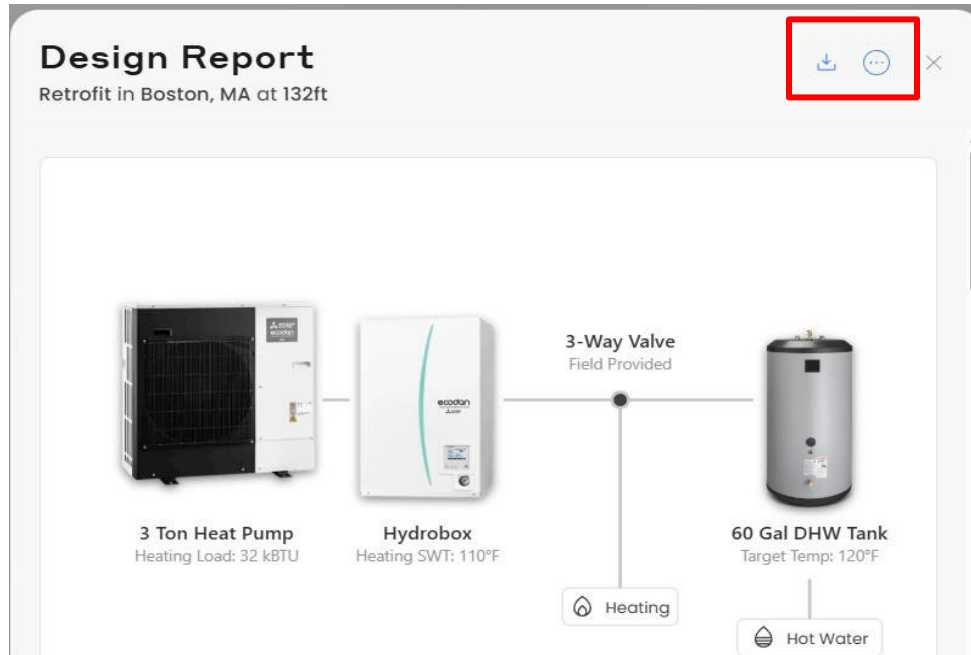

1. If you select the ellipsis icon you will get a few additional options in addition to the option to download the PDF.

- C. Save the downloaded PDF to the email in next steps

III. Complete the installation and the Ecodan® Startup Checklist

- A. Complete the Startup Checklist provided at the end of this document
 1. Be sure to include the following:
 - a. Customer Name and Address
 - b. Installation and Startup Date
 - c. Contractor Name and Address
 - d. Contractor Employee who has completed Ecodan® Essentials Training
 - e. Model and Serial numbers or Ecodan®, Hydrobox and Heat-flo storage tanks (if applicable)
 - f. Complete other checklist items regarding the installation and operation of the product



g. Save the completed checklist

IV. Submitting Extended Warranty Documents

- A. Email the two required files to cmwarranty@hvac.mea.com within 90 days of startup.
- B. If you have any questions regarding collection of data and submission you can contact the warranty department at cmwarranty@hvac.mea.com.



Residential Ecodan® Installation & Startup Checklist

PROJECT INFORMATION

Project / Owner Name:			
Address:			
City / State / Zip code:			
Contractor Name:		Install Date:	
Trained Employee Name:		Startup Date:	

EQUIPMENT INFORMATION

Outdoor Model / Service Reference Number		Serial Number	
Hydrobox Model / Service Reference Number		Serial Number	
Indirect Hot Water Tank Model / Service Reference Number		Serial Number	
Outdoor Model / Service Reference Number		Serial Number	
Hydrobox Model / Service Reference Number		Serial Number	
Indirect Hot Water Tank Model / Service Reference Number		Serial Number	

INSTALLATION

☐	Minimum operational and service clearances maintained according to installation instructions
☐	Unit secured properly to approved mounting supports
☐	Proper spacing has been provided for face-to-face and side-by-side layouts
☐	The system is adequately protected from Freezing and pipes insulated to prevent heat loss
☐	The refrigerant circuit has been evacuated and charged in accordance with manufacturer's instructions

WATER PIPING

☐	Water quality has been tested and meets the Mitsubishi Electric Ecodan® model ERSF (Hydrobox) Installation Manual
☐	System piping has been flushed, then adequately filled to meet primary side pressure requirements
☐	Expansion tank for heating is sized, fitted, and charged in accordance with manufacturer's instructions
☐	Systems water piping meets minimum volume requirements and is verified leak free
☐	Ensure both Hydrobox pressure relief valve connections are completed and terminated to meet all applicable codes
☐	Confirm water strainers have been cleaned and ready for operation



MITSUBISHI ELECTRIC TRANE HVAC US

1340 Satellite Blvd.
Suwanee, GA 30024

COMPONENTS

☐	Air separator cap is loose for air relief
☐	Set Flow Switch
☐	Set Circulator Pump
☐	Set System Feeder (if applicable)
☐	Expansion Tank properly sized and PSI Set
☐	Dielectric Protection has been installed at water inlet and outlets of unit
☐	

ELECTRICAL

☐	Verify electrical circuits meet NEC requirements and recommended fuse sizes
☐	Measure line voltage and verify it is within nameplate minimum to maximum rating
☐	Verify wiring connections are secure and correct
☐	Proper line voltage is connected to circulator pumps
☐	Proper line voltage is connected to Heat Trace (if required)
☐	Verify pumps are connected to correct terminal on TB01
☐	Verify field installed flow switches are connected to correct TBI.1 terminals
☐	Verify wiring is correct for field installed mixing valve (if applicable)
☐	

CONTROLS WIRING (LOW VOLTAGE)

☐	Confirm input wiring for Room temperature thermostat TBI.1:7-8
☐	Confirm input wiring for DHW tank temperature thermistor THW5B is wired to CNW5 connector
☐	Confirm input thermistor THW6 wiring for zone 1 supply water temperature is connected to TBI.5:7-8
☐	Confirm Input thermistor THW7 wiring for zone 1 return water temperature is connected to TBI.5:5-6
☐	Confirm all thermistors are properly located, installed, and secured per the Installation Manual for Hydrobox

SYSTEM CONFIGURATION PROCEDURE

☐	Outdoor unit to be powered up 12-24 hours before startup
☐	Confirm set-up details with Quick Start Guide, Installation Manual, and Service Manual
☐	Confirm Dip Switch Settings with Quick Start Guide, Installation Manual, and Service Manual

Signature of Agent: _____, Title: _____, Date Completed: _____
